Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Res	Total Float
Monroe Elem School		344		11-Sep-17	03-Jan-19		-10
General Conditions		44		29-Sep-17	30-Nov-17		0
A1670	Mix Design Submittal Approved	0	0%		29-Sep-1		0
A1690	Mobilization	10	0%	02-Oct-17*	13-Oct-17		-10
A1600	Rebar Shop Drawings Approved/Released	0	0%		04-Oct-1		-10
A1030	Hollow Metal Frames Submittal Approved	0	0%		06-Oct-1		0
A1590	Masonry Submittals Approved	0	0%		13-Oct-1		0
A1010	Steel/Joists Submittals Approved	0	0%		10-Nov-1		0
A1680	Elevator Submittal Approved	0	0%		30-Nov-1		0
Phase 1 - Site/Geothermal		0		18-Oct-17	18-Oct-17		0
A1040	Estimated Sitework and Geothermal Complet	0	0%		18-Oct-1		0
Phase 2 - Two Story Classroom Addition		287		03-Oct-17	07-Nov-18		0
Level 1		276		03-Oct-17	23-Oct-18		11
A1420	Building Shell Start	0	0%	03-Oct-17*			0
A1410	Excavate/Pour Footers	25	0%	06-Nov-17	08-Dec-17		16
A1450	Systems/Finishes Start	0	0%	20-Nov-17*			0
A1430	Foundation Walls	15	0%	11-Dec-17	29-Dec-17		16
A1440	SOG	15	0%	01-Jan-18	19-Jan-18		41
A1460	CMU Walls	40	0%	22-Jan-18	16-Mar-18		1
A1520	Structural Steel Set	20	0%	19-Mar-18	13-Apr-18		1
A1700	Paint	12	0%	09-Jul-18	24-Jul-18		11
A1710	Finishes(Grid, Tile, Floors, Casework)	65	0%	25-Jul-18	23-Oct-18		11
Level 2		158		02-Apr-18	07-Nov-18		0
A1580	Level 2 CMU Walls	30	0%	02-Apr-18	11-May-1		1
A1720	Level 2 Metal Decking	10	0%	30-Apr-18	11-May-1		36
A1470	Joist/Misc. Steel	15	0%	14-May-18	01-Jun-18		1
A1480	Roof Deck	15	0%	04-Jun-18	22-Jun-18		1
A1610	SOD	15	0%	14-Jun-18	04-Jul-18		13
A1490	Spray Foam	10	0%	25-Jun-18	06-Jul-18		11
A1500	Roof	20	0%	25-Jun-18	20-Jul-18		1
A1020	Building Shell Finish	0	0%		27-Jun-1		0
A1510	Brick	40	0%	09-Jul-18	31-Aug-18		33
A1530	Paint	12	0%	23-Jul-18	07-Aug-18		1
A1540	Finishes(Grid, Tile, Floors, Casework)	65	0%	08-Aug-18	06-Nov-18		1
A1550	Windows	15	0%	03-Sep-18	21-Sep-18		33
A1560	Systems/Finishes Finish	0	0%		07-Nov-1		0
A1570	Substantial Completion	0	0%		07-Nov-1		0
Phase 3 - Gym/Kitchen/Cafe		344		11-Sep-17	03-Jan-19		-10
Gym Addition		229		11-Sep-17	26-Jul-18		0
A1180	Building Shell Start	0	0%	11-Sep-17*			-6
A1220	Pending Overhead Elec. Utility Relo	0	0%		04-Oct-1		-3
A1050	Excavate/Pour Footers	25	0%	16-Oct-17	17-Nov-17		-10
A1060	Foundation Walls	15	0%	20-Nov-17	08-Dec-1		-10
A1190	Systems/Finishes Start	0	0%	20-Nov-17*			0
A1070	SOG	15	0%	11-Dec-17	29-Dec-17		37
A1080	CMU Walls	40	0%	11-Dec-17	02-Feb-18		-3
A1100	Joist/Misc. Steel	15	0%	05-Feb-18	23-Feb-18		-3
A1110	Roof Deck	10	0%	26-Feb-18	09-Mar-18		-3
A1090	Spray Foam	10	0%	12-Mar-18	23-Mar-18		9
A1120	Roof	15	0%	12-Mar-18	30-Mar-18		-3
A1130	Brick	40	0%	26-Mar-18	18-May-1		34
A1170	Building Shell Finish	0	0%		30-Mar-1		-3
A1150	Paint	15	0%	02-Apr-18	20-Apr-18		4
A1160	Finishes/Finish Equipment	65	0%	23-Apr-18	20-Jul-18		4
A1140	Windows	15	0%	21-May-18	08-Jun-18		34
A1200	Systems/Finishes Finish	0	0%		26-Jul-18*		0
A1210	Substantial Completion	0	0%		26-Jul-18*		0
Kitchen/Cafeteria		179		30-Apr-18	03-Jan-19		-10
A1250	Building Shell- Start per milestone sched. Ca	0	0%	30-Apr-18*			0
A1230	Demo	15	0%	01-Jun-18*	21-Jun-18		-10
A1660	Stone SOG Fill/Grade	15	0%	22-Jun-18	12-Jul-18		-10
A1280	Systems/Finishes Start	0	0%	06-Jul-18*			0
A1240	Excavate/Pour Footers	15	0%	13-Jul-18	02-Aug-18		-10
A1260	Foundation Walls	10	0%	03-Aug-18	16-Aug-18		-10
A1270	SOG	10	0%	17-Aug-18	30-Aug-18		5
A1290	CMU Walls	25	0%	17-Aug-18	20-Sep-18		-10
A1350	Building Shell Finish	0	0%		12-Sep-1		0
A1300	Joist/Misc. Steel	10	0%	21-Sep-18	04-Oct-18		-10
A1310	Roof Deck	10	0%	05-Oct-18	18-Oct-18		-10
A1320	Spray Foam	10	0%	19-Oct-18	01-Nov-18		0
A1330	Roof	15	0%	19-Oct-18	08-Nov-18		-10
A1340	Brick	20	0%	02-Nov-18	29-Nov-18		0
A1360	Paint	10	0%	09-Nov-18	22-Nov-18		-10
A1370	Finishes	30	0%	23-Nov-18	03-Jan-19		-10
A1380	Windows	15	0%	30-Nov-18	20-Dec-18		0
A1390	Systems/Finishes Finish	0	0%		21-Dec-1		-1
A1400	Substantial Completion	0	0%		03-Jan-1		-10
Phase 4 - Renovation/Office Addition		133		01-Jun-18	11-Oct-18		0
Addition		133		01-Jun-18	11-Oct-18		0
A1620	Addition Start	0	0%	01-Jun-18*			0
A1630	Addition Completion	0	0%		11-Oct-1		0
Renovation		88		01-Jun-18	27-Aug-18		0
A1640	Renovation Start	0	0%	01-Jun-18*			0
A1650	Renovation Completion	0	0%		27-Aug-1		0

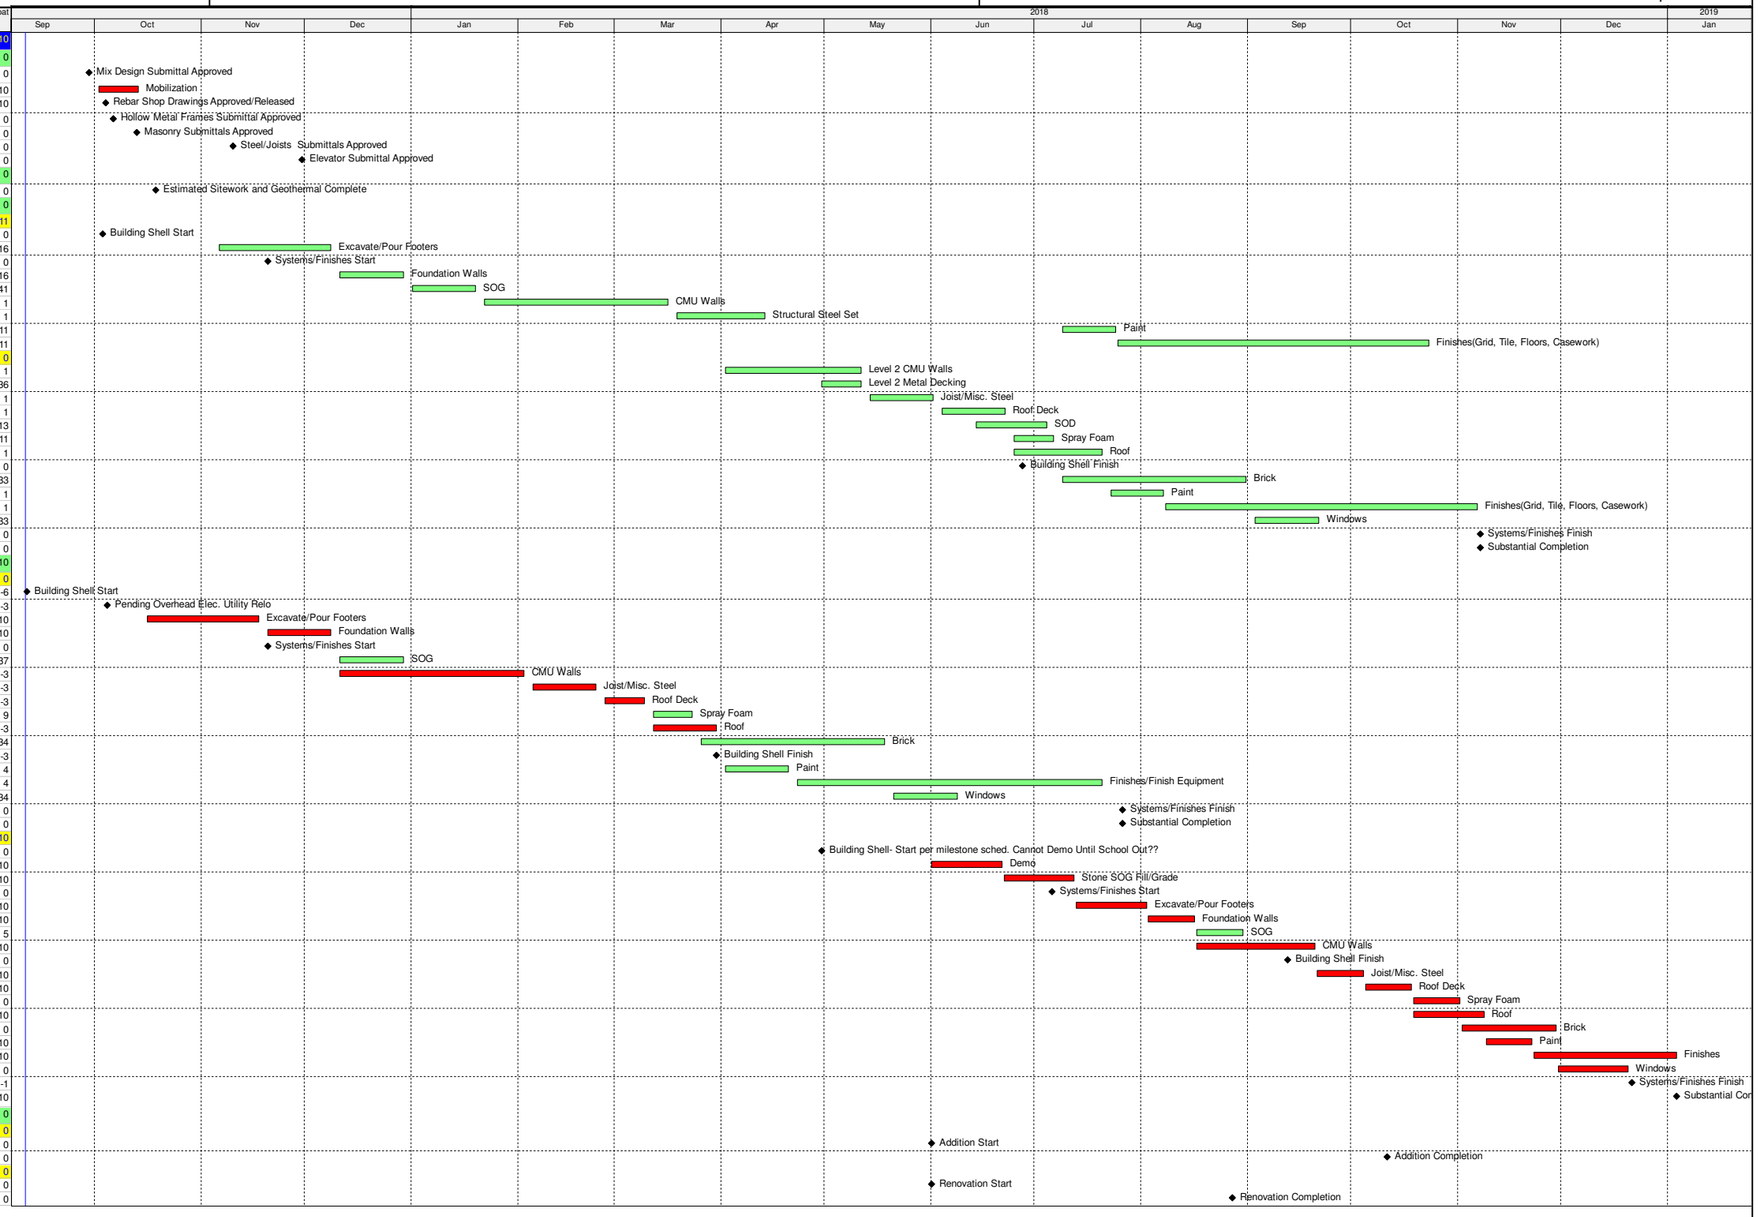

Actual Work | Critical Remaining Work | Remaining Work | Milestone
